



Strategic Irrigation Modernization and Urgent Rehabilitation Project (P157585)

EAST ASIA AND PACIFIC | Indonesia | IBRD/IDA | Investment Project Financing (IPF) | FY 2018 | Seq No: 17 | Archived on 27-Jun-2025 | ISR04264

1. OBJECTIVE

1.1 Development Objective

Original Development Objective (Approved as part of Approval package on 21-Jun-2018)

The Project Development Objective is to improve irrigation services and strengthen accountability of irrigation schemes management in selected areas.

Has the Development Objective been changed since Board Approval of the Project Objective?

No

2. COMPONENTS

Name
Component A: Urgent Rehabilitation of Irrigation and Drainage System:(Cost 306,400,000.00)
Component B: Strategic Modernization of Irrigation and Drainage System:(Cost 221,500,000.00)
Component C: Project Management:(Cost 17,100,000.00)

3. OVERALL RATINGS

Name	Previous	Current
Progress towards achievement of PDO	● Satisfactory	● Satisfactory
Overall Implementation Progress (IP)	● Satisfactory	● Moderately Satisfactory
Overall Risk Rating	● Moderate	● Moderate

4. KEY ISSUES & STATUS

4.1 Implementation Status and Key Decisions



The project managed to improve irrigation services to cover an area of 274,155 Hectares in Sei Ular, Karang Agung Hilir, Cipancuh, Cikeusik, Kedung Putri, Wadaslintang, Jengkelok, Sempor, Glapan Timur, Banjarcayana, Talang, Pondok Waluh, Pamukkulu, Jurang Batu, Katingan, Saddang, Ameroro, San Rego, Tabo-Tabo, Jatiluhur SS Macan, Jatiluhur SS Pamanukan, and Talang BTT. This has resulted in 14% increase in crop intensity. The establishment, revitalization and legalization of Water User Association (WUAs) has been completed, up to 1,207 WUAs under Component A (Urgent Rehabilitation of Irrigation and Drainage System) and up to 1,826 WUAs under Component B (Strategic Modernization of Irrigation and Drainage System) have been strengthened. Thirty Irrigation Commissions (KOMIR) have been established and are functional under Component A and B.

A key innovation under the project is the preparation and signing of Irrigation Service Agreements (ISAs), with 13 signed between the WUAs and River Basin Organizations (RBOs). These ISAs aim to enhance the accountability and quality of irrigation services by describing the processes, rights and obligations of RBOs and WUAs regarding water allocation and delivery.

5. SYSTEMATIC OPERATIONS RISK-RATING TOOL

Risk Category	Rating at Approval Approval Package - 21 Jun 2018	Last Approved Rating ISR Seq. 016 - 06 Feb 2025	Proposed Rating
Political and Governance	● Moderate	● Moderate	● Moderate
Macroeconomic	● Moderate	● Moderate	● Moderate
Sector Strategies and Policies	● Substantial	● Moderate	● Moderate
Technical Design of Project or Program	● Substantial	● Moderate	● Moderate
Institutional Capacity for Implementation and Sustainability	● High	● Moderate	● Moderate
Fiduciary	● High	● Substantial	● Substantial
Environment and Social	● Moderate	● Moderate	● Moderate
Stakeholders	● Substantial	● Moderate	● Moderate
Overall	● Substantial	● Moderate	● Moderate



6. RESULTS

6.1 PDO Indicators by PDO Outcomes

Improvement of irrigation services								
Indicator Name	Baseline		Actual (Previous)		Actual (Current)		Closing Period	
	Value	Month/Year	Value	Date	Value	Date	Value	Month/Year
Area provided with new/improved irrigation or drainage services (Hectare(Ha))	0.00	Jul/2018	270,259	15-Jan-2025	274,155	30-May-2025	253,102.00	Jun/2024
Area provided with new/improved irrigation or drainage services (Hectare(Ha))	0.00	Jul/2018	270,259	15-Jan-2025	274,155	30-May-2025	253,102.00	Jun/2024
Percentage of crop intensity (paddy) (Percentage)	180.00	Jul/2018	216	15-Jan-2025	216	30-May-2025	200.00	Jun/2024
Strengthened accountability of irrigation schemes management								
Indicator Name	Baseline		Actual (Previous)		Actual (Current)		Closing Period	
	Value	Month/Year	Value	Date	Value	Date	Value	Month/Year
Number of irrigation service agreements with clear allocation of responsibilities implemented. (Number)	0.00	Jul/2018	13	15-Jan-2025	13	15-Jan-2025	9.00	Jun/2024
Number of asset management systems with transparent budget allocation operational (Number)	0.00	Jul/2018	18	15-Jan-2025	18	15-Jan-2025	9.00	Jun/2024



6.2 Intermediate Results Indicators by Components

Component A: Urgent Rehabilitation of Irrigation and Drainage System								
Indicator Name	Baseline		Actual (Previous)		Actual (Current)		Closing Period	
	Value	Month/Year	Value	Date	Value	Date	Value	Month/Year
Annual performance report of irrigation service providers published (Component A) (Number)	0.00	Jul/2018	11.00	15-Jan-2025	11.00	30-May-2025	8.00	Jun/2024
Irrigation Commission (KOMIR) established and operational (Component A) (Number)	8.00	Jul/2018	27.00	15-Jan-2025	27.00	30-May-2025	24.00	Jun/2024
Participatory Irrigation Development and Management (PPISP) included in planning documents (Component A) (Number)	9.00	Jul/2018	30.00	15-Jan-2025	30.00	30-May-2025	19.00	Jun/2024
WUAs with trained members in decision making (Component A) (Number)	0.00	Jul/2018	1,207.00	15-Jan-2025	1,207.00	30-May-2025	390.00	Jun/2024
WUAs with trained female members in decision making (Component A) (Percentage)	0.00	Jul/2018	66.00	15-Jan-2025	79	30-May-2025	50.00	Jun/2024



Number of WUAFs established and operational (Component A) (Number)	0.00	Jul/2018	145	15-Jan-2025	171	30-May-2025	90.00	Jun/2024
Establishment and operationalization of grievance mechanism for water users in delivery of irrigation services (Component A) (Number)	0.00	Jul/2018	12.00	15-Jan-2025	12.00	30-May-2025	6.00	Jun/2024
Number of farmer households provided with improved irrigation services (Component A) (Number (Thousand))	0.00	Jul/2018	515	18-Jul-2024	515	30-May-2025	429.00	Jun/2024
Component B: Strategic Modernization of Irrigation and Drainage System								
Indicator Name	Baseline		Actual (Previous)		Actual (Current)		Closing Period	
	Value	Month/Year	Value	Date	Value	Date	Value	Month/Year
Annual performance report of irrigation service providers published (Component B) (Number)	0.00	Jul/2018	1.00	15-Jan-2025	1.00	30-May-2025	1.00	Jun/2024
Irrigation Commission (KOMIR) established and operational (Component B) (Number)	1.00	Jul/2018	3.00	15-Jan-2025	3.00	30-May-2025	3.00	Jun/2024
Participatory Irrigation Development and Management (PPISP) included in planning	1.00	Jul/2018	4.00	15-Jan-2025	4.00	30-May-2025	2.00	Jun/2024




documents (Component B) (Number)								
WUAs with trained members in decision making (Component B) (Number)	0.00	Oct/2018	1,826.00	15-Jan-2025	1,826.00	30-May-2025	480.00	Jun/2024
WUAs with trained female members in decision making (Component B) (Percentage)	0.00		100.00		100.00		50.00	
Number of WUAFs established and operational (Component B) (Number)	0.00	Jul/2018	182	15-Jan-2025	182	30-May-2025	160.00	Jun/2024
Establishment and operationalization of grievance mechanism for water users in delivery of irrigation services (Component B) (Number)	0.00	Apr/2022	1.00	15-Jan-2025	1.00	30-May-2025	1.00	Jun/2024
Number of farmer households provided with improved irrigation services (Component B) (Number (Thousand))	0.00	Jul/2018	381	15-Jan-2025	381	30-May-2025	362.00	Jun/2024



7. DATA ON FINANCIAL PERFORMANCE

7.1 Cumulative Disbursements

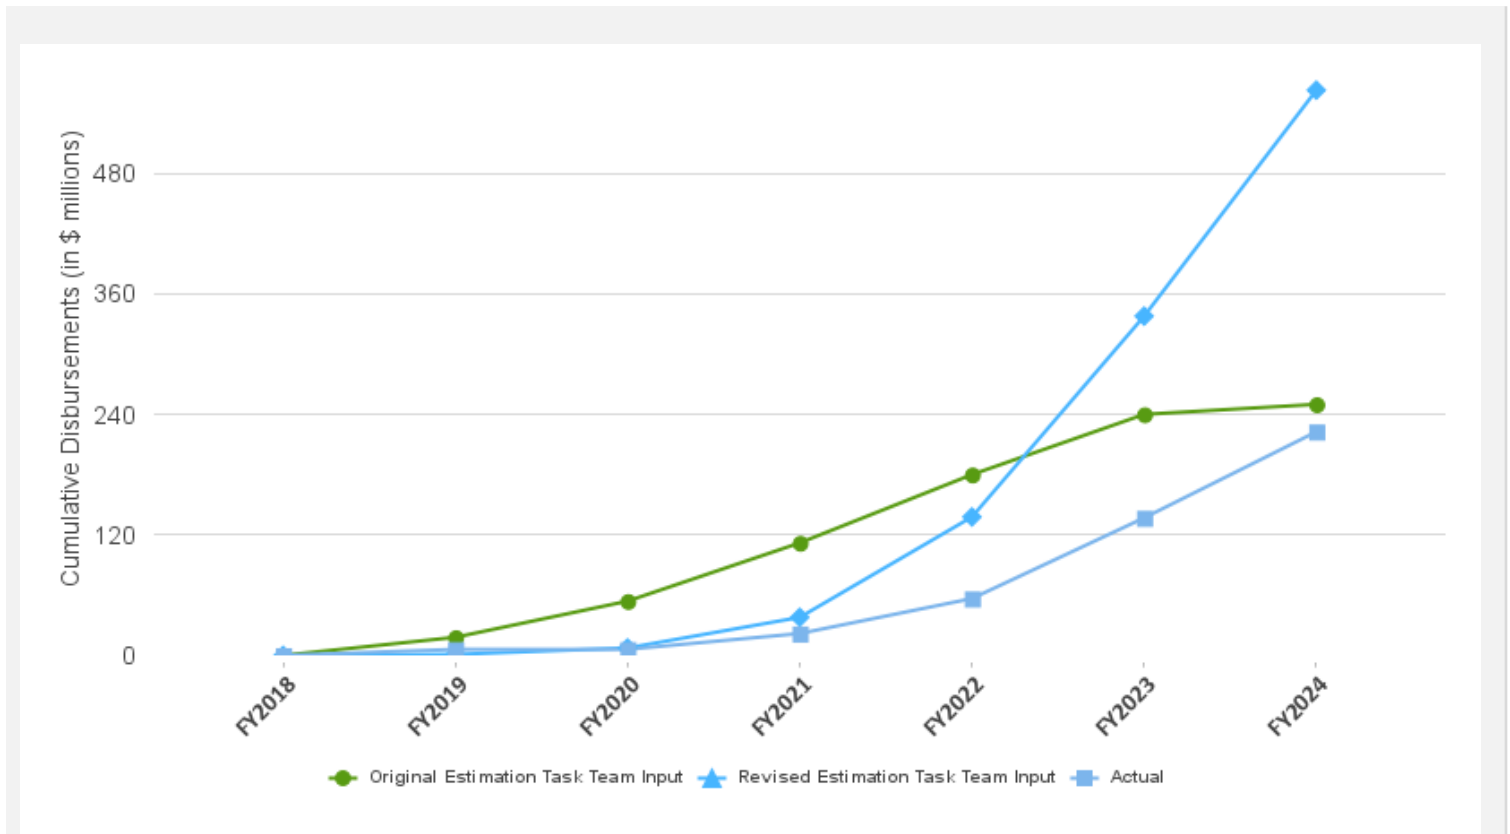

7.2 Disbursements (by loan)

Loan/Credit/TF	Status	Original	Revised	Cancelled	Disbursed	Undisbursed	% Disbursed
IBRD-88910	Effective	250.00	250.00	0.00	244.76	5.24	97.91%

7.3 Key Dates (by loan)

Loan/Credit/TF	Status	Approval	Signing	Effectiveness	Orig. Closing	Rev. Closing
IBRD-88910	Effective	21-Jun-2018	25-Jul-2018	23-Aug-2018	30-Jun-2024	30-Jun-2025

8. KEY DATES



Key Events	Planned	Actual
Approval	21-Jun-2018	21-Jun-2018
Effectiveness	23-Aug-2018	23-Aug-2018
Mid-Term Review No. 01	19-Jul-2021	24-Aug-2021
Operation Closing/Cancellation	30-Jun-2025	

9. RESTRUCTURING HISTORY

Restructuring Level 2 Approved on 22-Apr-2022

Restructuring Level 2 Approved on 05-Jun-2024

10. ASSOCIATED OPERATION(S)

There are no associated operations
