



Digital Acceleration Project (P173373)

EASTERN AND SOUTHERN AFRICA | Rwanda | IBRD/IDA | Investment Project Financing (IPF) | FY 2022 | Seq No: 9 |
Archived on 13-May-2026 | ISR07584

Implementing Agencies: Development Bank of Rwanda, National Identification Agency (NIDA), Rwanda Information Society Authority

1. OBJECTIVE

1.1 Development Objective

Original Development Objective (Approved as part of Approval package on 30-Nov-2021)
To increase access to broadband and selected digital public services, and strengthen the digital innovation ecosystem

Has the Development Objective been changed since Board Approval of the Project Objective?

No

2. COMPONENTS

Name
Digital Access and Inclusion:(Cost 53,400,000.00)
Digital Public Service Delivery:(Cost 125,000,000.00)
Project Management and Institutional Coordination:(Cost 8,000,000.00)
Digital Innovation and Entrepreneurship:(Cost 13,600,000.00)

3. OVERALL RATINGS

Name	Previous	Current
Progress towards achievement of PDO	● Moderately Satisfactory	● Moderately Satisfactory
Overall Implementation Progress (IP)	● Moderately Satisfactory	● Moderately Satisfactory
Overall Risk Rating	● Moderate	● Moderate



4. KEY ISSUES & STATUS

4.1 Implementation Status and Key Decisions

The Rwanda Digital Acceleration Project (RDAP) has made significant progress since the last implementation support mission, with notable gains across all major components. The project is exceeding targets for the number of people benefitting from new or enhanced access to the Internet, digital literacy, access to e-services and support for digital startups, reflecting the impact of ongoing investments in connectivity, digital platforms and skills and entrepreneurship programs. A restructuring was processed in March 2026 to restore US\$20m in funding that was previously cancelled due to a temporary reduction in the IDA financing envelope. This will enable the achievement of the project’s core objectives and results.

Under component 1, the project is registered significant advancements in connecting Rwandans to broadband, adding 1.2 million new users between November 2025 and March 2026, and overshooting the target of 2 million by 277 thousand. The Digital Ambassadors Program (DAP), under sub-component 1.2, trained an additional 309 thousand people, reaching a total of 2.8 million people trained (52% women and 48% men) as of March 2026 and the target was revised upward to 3.8 million.

Under component 2, mass enrollment for Rwanda's new Single Digital ID (SDID) system began on October 28, 2026, and as of March 2026 19% of the population had been enrolled, up from 1.67% in November 2025. Strong public turnout and efficient processing have kept the National Identification Agency (NIDA) on track to meet enrollment goals. Other key achievements include the digitalization of over 10 million paper-based records, bringing the total to 11,117,244 (89% of target).

Under component 3, significant progress has been made in supporting digitally skilled talent, digital start-ups and entrepreneurship support organizations. The Early-Stage Finance Facility (ESF) funded and additional 6 companies, bringing the total to 28, spread across sectors such as FinTech, ClimateTech, HealthTech, AgTech, Mobility, Logistics, and AI/ML. Three additional cohorts are planned to reach the 40-company target by June 2026. A total of 78 startups – nearly double the revised target of 40 – are expected to benefit from the component. Two cohorts totaling 176 students have been selected for student loans for advanced digital degree programs, with 128 (including 42% women) currently receiving support. Moreover, 178 students have graduated from the Rwanda Coding Academy.

Looking ahead, key priorities include distributing 20,000 broadband-enabled devices, scaling SDID enrollment and operationalization, and establishing the Government Data Hub with cybersecurity and data protection capacity. These are critical foundations for AI readiness and adoption. The project remains well positioned to achieve its development objectives and support Rwanda’s broader digital and AI-enabled transformation.

5. SYSTEMATIC OPERATIONS RISK-RATING TOOL

Risk Category	Rating at Approval	Last Approved Rating	Proposed Rating
	Approval Package - 30 Nov 2021	AF Seq. 01 Approval - 30 Mar 2026	



Political and Governance	● Low	● Low	● Low
Macroeconomic	● Moderate	● Moderate	● Moderate
Sector Strategies and Policies	● Moderate	● Moderate	● Moderate
Technical Design of Project or Program	● Moderate	● Moderate	● Moderate
Institutional Capacity for Implementation and Sustainability	● Substantial	● Moderate	● Moderate
Fiduciary	● Moderate	● Substantial	● Substantial
Environment and Social	● Moderate	● Moderate	● Moderate
Stakeholders	● Moderate	● Moderate	● Moderate
Overall	● Moderate	● Moderate	● Moderate



6. RESULTS

6.1 PDO Indicators by PDO Outcomes

Increase Access to Broadband								
Indicator Name	Baseline		Actual (Previous)		Actual (Current)		Closing Period	
	Value	Month/Year	Value	Date	Value	Date	Value	Month/Year
People using broadband internet (new use) (Number of people) CRI	0	Dec/2021	1,075,065	01-Nov-2025	1,075,065	31-Mar-2026	2,000,000	Jun/2028
	Comments on achieving targets		About 750 schools were connected between May and November 2025, driving the increase in this indicator. New new schools connected during the current reporting period. Methodology based on updated CRI methodology. Upcoming connectivity interventions will target additional new users, with the project on track to achieve targets by project closure.					
People using broadband internet (new use) - Female (Number of people) CRI	0	Dec/2021	536,899	01-Nov-2025	536,899	31-Mar-2026	1,000,000	Jun/2028
	Comments on achieving targets		Figure is lower than in the previous ISR due to updated methodology whereby more users are counted under enhanced use rather than new use					
People using broadband internet (new use) - Youth (Number of people) CRI	0	Dec/2021	1,028,741	01-Nov-2025	1,028,741	31-Mar-2026	400,000	Jun/2028
	Comments on achieving targets		Methodological adjustment to count 95% of all school users as youth driving the change in this indicator. This will be the approach going forward.					
People using broadband internet (inferred use) (Number of people) CRI			0	01-Nov-2025	0	31-Mar-2026	0	Jun/2028
	Comments on achieving targets		Based on the current CRI methodology, no inferred usage is expected. While the project will be deploying fiber along energy transmission lines the results will likely only be registered after the closing date. The indicator is currently not counting inferred increase in broadband penetration expected due to delivery of targeted digital literacy training, but may do so in future based on the evolving methodology.					



People using broadband internet (inferred use) - Female (Number of people) CRI			0	01-Nov-2025	0	31-Mar-2026	0	Jun/2028
People using broadband internet (inferred use) - Youth (Number of people) CRI			0	01-Nov-2025	0	31-Mar-2026	0	Jun/2028
People using broadband internet (enhanced use) (Number of people) CRI	0	Dec/2021	1,206,200	01-Nov-2025	1,206,200	31-Mar-2026	500,000	Jun/2028
	Comments on achieving targets		Based on the CRI methodology, linked figures are based on the number of users in government buildings where the broadband connectivity has been upgraded via the project, including for universities and schools. The target set currently does not reflect current internet subscribers that would likely be benefiting from enhanced usage due to improvement in mobile internet speeds due to regulatory work and network investments made, and is thus conservative. Jump in figure since the last ISR is due to completion of relevant connectivity activities - whereby 1500 schools got enhanced internet capacity through Ubuntunet - and review of the calculation methodology whereby previously some of the enhanced users were erroneously captured under new users.					
People using broadband internet (enhanced use) - Female (Number of people) CRI	0	Dec/2021	566,200	01-Nov-2025	566,200	31-Mar-2026	250,000	Jun/2028
	Comments on achieving targets		Jump in figure since the last ISR is due to completion of relevant connectivity activities and review of the calculation methodology whereby previously some of the enhanced users were erroneously captured under new users.					
	0	Dec/2021	1,157,652	01-Nov-2025	1,145,890	31-Mar-2026	100,000	Jun/2028



People using broadband internet (enhanced use) - Youth (Number of people) CRI	Comments on achieving targets		Jump in figure since the last ISR is due to completion of relevant connectivity activities and review of the calculation methodology whereby previously some of the enhanced users were erroneously captured under new users. Methodology agreed that since all benefiting institutions are schools, 95% of users counted as youth.					
Increase Access to select Digital Public Services								
Indicator Name	Baseline		Actual (Previous)		Actual (Current)		Closing Period	
	Value	Month/Year	Value	Date	Value	Date	Value	Month/Year
Fully transactional G2P, G2B and G2G e-services that are introduced, upgraded, or enabled (Number)	0.00	Jun/2021	258	01-Nov-2025	258	31-Mar-2026	250	Jun/2028
	Comments on achieving targets		Planned work on e-procurement, e-notary and other systems is expect to contribute to increasing results further. Privately provided services on IREMBO are also included. Target adjusted upward as part of March 2026 AF as previous one had been achieved.					
Strengthen the Digital Innovation Ecosystem								
Indicator Name	Baseline		Actual (Previous)		Actual (Current)		Closing Period	
	Value	Month/Year	Value	Date	Value	Date	Value	Month/Year
Digital startups supported creating and/or leveraging a digital technology solution (Number)	0.00	Dec/2021	72	01-Nov-2025	78	31-Mar-2026	40	Jun/2028
	Comments on achieving targets		Target updated as part of March 2026 AF. Results logged reflect digital startups which have been supported via industry/fundraising events, through ecosystem support organization (ESO) financed to provide enhanced coaching and business support services to startups ; and direct early-stage financing. More startups are set to benefit by project closing.					
Of which female-owned (Percentage)	0.00		16		18		30.00	
	Comments on achieving targets		Improved performance on gender target needed, through implementation of enhanced gender screening for all training and support activities going forward. This indicator will apply the IFC’s definition of women-owned enterprises, which includes firms where (i) a woman/women has/have a 51 percent or more ownership stake, or greater than or equal to 20 percent; (ii) 1 or more woman/women is/re the CEO/COO (President/Vice President); or (iii) 30 percent or more of the board of directors are women.					



6.2 Intermediate Results Indicators by Components

Digital Access and Inclusion								
Indicator Name	Baseline		Actual (Previous)		Actual (Current)		Closing Period	
	Value	Month/Year	Value	Date	Value	Date	Value	Month/Year
Beneficiaries that receive support under the smart device financing scheme (Number)	0.00	Dec/2021	0.00	01-Nov-2025	0	31-Mar-2026	100,000.00	Jun/2028
	Comments on achieving targets		Progress on track. Provider selected under the subsidy window of the Device Access Fund (DAF). Registration of eligible end-beneficiaries is ongoing. Distributions of subsidized smart devices is expected to begin in January 2026 to at least 100,000 beneficiaries, placing the project on track to meet the target by closing.					
Of which persons with disabilities (Percentage)	0	Dec/2021	0	01-Nov-2025	0	31-Mar-2026	50	Jun/2028
	Comments on achieving targets		Supplemental indicator. This will be based on the provisions adopted in Ministerial Order N° 20/18 of 27/7/2009 which determines who is considered to be a person with disability in Rwanda. This will count those beneficiaries who have proved their status as a person with disability using one of the following means: via an ID disability card or medical certificate for permanent disability or a recommendation letter for persons with disabilities issued by the National Council of Persons with Disabilities through the Irembo platform.					
Of which female beneficiaries (Percentage)	0.00		0.00		0		50.00	
	Comments on achieving targets		Supplemental indicator.					
Of which beneficiaries in rural areas (Percentage)	0.00		0.00		0		30.00	
	Comments on achieving targets		Supplemental indicator. This will be based on the definition applied by the Integrated household Living Conditions Survey-EICV in respect to rural households.					
	0.00	Dec/2021	2,517,796	01-Nov-2025	2,826,993	31-Mar-2026	3,000,000.00	Jun/2028



People trained in digital literacy (Number)	Comments on achieving targets		On track to meet target					
Of which female (Percentage)	0.00		51		52		40.00	
	Comments on achieving targets		Target surpassed. Supplemental Indicator. Training participants who are female.					
Median mobile download speeds (in Mbps) (Number)	15.50	Dec/2021	34.90	01-Nov-2025	30	31-Mar-2026	45	Jun/2028
	Comments on achieving targets		Progress on track. The 50th percentile of end-user mobile download throughput measurements (in Mbps) collected during active speed tests over a specified reporting period, where throughput is calculated as the total number of successfully transferred data bits divided by the total transfer time across the test interval, excluding control overhead					
Internet access points established benefiting from new or enhanced broadband connectivity (connected govt. offices, schools, hospital etc.) (Number)	0.00	Dec/2021	3,054	01-Nov-2025	3,054	31-Mar-2026	5,000.00	Jun/2028
	Comments on achieving targets		The number of sites connected with new or enhance internet capacity currently include mainly universities and secondary schools as well as some new health facilities connected. Many more government offices are due to benefit over the course of the next few months, placing the project on track to surpass the target set.					
Of which located in rural areas (Percentage)	0.00		75		69		75.00	
	Comments on achieving targets		Supplemental indicator. This will be based on the definition applied by the Integrated household Living Conditions Survey-EICV in respect to rural versus urban areas. Sites in the pipeline are expected to increase rural coverage.					
Digital Public Service Delivery								
Indicator Name	Baseline		Actual (Previous)		Actual (Current)		Closing Period	
	Value	Month/Year	Value	Date	Value	Date	Value	Month/Year
	0	Dec/2021	26,602	01-Nov-2025	105,575	31-Mar-2026	40,000	Jun/2028



People using digitally enabled services (new services) (Number of people) CRI	Comments on achieving targets		Results surpassed. Large increase since last ISR is due to adjustment in methodology to capture users of Irembo services through Agents. This captures users of new G2P and G2B services introduced, based on project activities, including new services added to Irembo. Based on the CRI methodology, new G2G services financed by the project are not counted.					
People using digitally enabled services (new services) - Female (Number of people) CRI	0	Dec/2021	7,937	01-Nov-2025	9,474	31-Mar-2026	17,200	Jun/2028
People using digitally enabled services (new services) - Youth (Number of people) CRI	0	Dec/2021	5,366	01-Nov-2025	0	31-Mar-2026	8,000	Jun/2028
	Comments on achieving targets		Irembo does not capture users' age, so reporting is not possible at this stage.					
People using digitally enabled services (enhanced services) (Number of people) CRI	0	Dec/2021	299,152	01-Nov-2025	7,960,856	31-Mar-2026	500,000	Jun/2028
	Comments on achieving targets		Target surpassed. Large increase as previous reported numbers did not count users sing Irembo services through Agents. Confirmed individual users per service e.g. if a user X applied for birth certificate 5 times, she/he is counted once but if he applied for a birth certificate, a marriage certificate, a land transfer, and paid for traffic fine, she/he is counted as 4 users. This captures users of G2P and G2B services that have been upgraded, based on project activities, including services enhanced on Irembo. Based on the CRI methodology, enhanced G2G services financed by the project are not counted.					
People using digitally enabled services (enhanced services) - Female (Number of people) CRI	0	Dec/2021	128,635	01-Nov-2025	2,164,087	31-Mar-2026	215,000	Jun/2028
	Comments on achieving targets		Target surpassed. Large increase as previous reported numbers did not count users sing Irembo services through Agents.					



People using digitally enabled services (enhanced services) - Youth (Number of people) CRI	0	Dec/2021	60,338	01-Nov-2025	16,369	31-Mar-2026	100,000	Jun/2028
Number of paper-based records digitalized (Number)	0	Dec/2021	900,000	01-Nov-2025	11,117,244	31-Mar-2026	12,500,000	Jun/2028
	Comments on achieving targets		Progress on track. Digitalization of civil record is underway. Jump in number due to erroneous reporting in last reporting period whereby November 2025 numbers should have been 9 million, not 900,000.					
Population enrolled in new digital ID system (Percentage)	0.00	Dec/2021	1.67	01-Nov-2025	19	31-Mar-2026	75.00	Jun/2028
	Comments on achieving targets		Progress on track. Mass enrollment in the new digital ID system began in October 2025, following initial testing, deployment of registration kits, development of pre-enrollment and registration systems. Enrollment began in Gisagara, Huye, and Nyanza. To date, approximately 1.67% of the population has been registered. However, based on strong public turnout, supported by a targeted communications campaign, and the average processing time recorded, NIDA is on track to meet its enrollment targets. The target is based on the total population estimated by 2026 which is expected to be roughly 14 million. 75% would thus be equivalent to 10.5 million.					
Of which female (Percentage)	0.00		0.00				40.00	
	Comments on achieving targets		Target surpassed. Supplement indicator. This indicator refers to the share of those enrolled who are women.					
Children enrolled (Percentage)	0.00		1.00		5.20		50.00	
	Comments on achieving targets		Supplement indicator. This indicator refers to the share of the total population, who are between 5-18 years of age, who have been enrolled in the new ID system. The total child population is 42% of 14 million is 5.9 million. 50% would therefore be 2.9 million.					
	No	Dec/2021	No	01-Nov-2025	No	31-Mar-2026	Yes	Jun/2028



Upgrade of SOC and Disaster Recovery Site completed (Yes/No)	Comments on achieving targets		Indicator to be updated. In view of progress expected in upgrading the CSIRT, which will boost Government's cyber resilience, it was agreed that this would be a more impactful indicator—replacing the existing cyber audit framework (which may be done in-house)—to be amended as part of the forthcoming additional financing process.					
Public sector officials trained in digital skills (Number)	0.00	Dec/2021	907	01-Nov-2025	806	31-Mar-2026	600.00	Jun/2028
	Comments on achieving targets		Target surpassed. Reduction in number from last reporting period is due to change in methodology whereby only completed trainings are now counted. Considerable progress has been made in upskilling the civil service for the safe and effective management of digital systems and services. Government employees have been trained on topics such as data protection and ISO risk management. Approximately half of trainings completed have resulted in industry-recognized certifications. Additional training is planned before project closing that will increase results further.					
People accessing new e-services supported through the project and reporting satisfaction (Percentage)	0.00	Dec/2021	87.40	01-Nov-2025	87.40	31-Mar-2026	75.00	Jun/2028
	Comments on achieving targets		Target surpassed. This records the “Level of citizen satisfaction with IREMBO services” according to the Governance Scorecard, published by the Rwanda Governance Board, on 31 Oct 2025. It reflects improvements made to Irembo 3.0 - the main e-services portal - through the project since work started on the upgrade of the platform in 2024.					
Data Controllers and Processors that are listed in the DPO Register (Number)	0.00	Dec/2021	0	01-Nov-2025	0	31-Mar-2026	100.00	Jun/2028
	Comments on achieving targets		Progress delayed but on track. Data Controllers and Processors are currently registered in a simplified non-digital format, with 2,500 already registered. These will be transfer to a digital registry being contracted, allowing the project to register results by March 2026.					
Datasets available for download in the Government Data Hub (Number)	0.00	Dec/2021	0.00	01-Nov-2025	0	31-Mar-2026	400.00	Jun/2028
	Comments on achieving targets		Progress delayed but on track. The Data Hub is currently being procured. Implementation of the data hub is expected to begin in early 2026 and be completed by closing, allowing the target to be met by project closing.					
	0.00	Dec/2021	0.00	01-Nov-2024	0	31-Mar-2026	15.00	Jun/2028



People issued and actively using digital ID credentials (Percentage)	Comments on achieving targets		ID credential issuance is expected to start in early 2026, based on the first round of enrollment conducted at the end of 2025, which would allow for subsequent ID verification (usage). Because there is lag between enrollment, credential issues and subsequent usage the target is lower then for the proposed enrollment target based on what can realistically be registered by project closing. However, credential issuance is expected to continue well beyond the closing date on the back of enrollment and systems investments made by the project.					
Of which female (Percentage)	0	Dec/2021			0	31-Mar-2026	40	Jun/2028
Children with ID (Percentage)	0	Dec/2021	0	01-Nov-2025			15	Jun/2028
Project Management and Institutional Coordination								
Indicator Name	Baseline		Actual (Previous)		Actual (Current)		Closing Period	
	Value	Month/Year	Value	Date	Value	Date	Value	Month/Year
New e-waste collection centers established and managed (Number)	0	Dec/2021	21	01-Nov-2025	24	31-Mar-2026	30	Jun/2028
	Comments on achieving targets		Progress on track. 21 out of 30 planned collection points now established. Establishment of remaining 9 centers are in progress, and thus expect by project closing. Enviroserve has collected some 233.67 tons of e-waste through these collection points nationwide. Awareness campaigns and training sessions on e-waste management have also been completed, supported by incentives provided to e-waste pickers operating across the country. To date, 140 e-waste pickers have been trained and supplied with personal protective equipment for safe collection. Additionally, 16 collection agents were recruited and trained to maintain the established collection points.					
Citizen engagement indicator:Grievances registered that receive an adequate response within 30 days (Percentage)	0.00	Dec/2021	100	01-Nov-2025	100	31-Mar-2026	75.00	Jun/2028
	Comments on achieving targets		Only one grievance registered to date and handled within the set timeline.					



Digital Innovation and Entrepreneurship								
Indicator Name	Baseline		Actual (Previous)		Actual (Current)		Closing Period	
	Value	Month/Year	Value	Date	Value	Date	Value	Month/Year
Startups receiving funding through the project (Number)	0.00	Dec/2021	22	01-Nov-2025	28	31-Mar-2026	40	Jun/2028
	Comments on achieving targets		Progress on track. Hanga Venture Ignite was launched in February 2025. 259 startups applied. A first cohort of 22 companies are benefitting from early-stage financing support (15 ignite+, 7 ignite) across diverse sectors including FinTech (5), ClimateTech (3), HealthTech (4), AgTech (2), Mobility (2), and Logistics (1) and AI/ML (4). Another cohort 5 is currently in screening, with approximately 20 additional companies targeted for funding by year-end to fully commit remainder of funds, placing BRD on track to meet the target for financed start-ups.					
People certified in advanced digital skills (Number of people)	0.00	Dec/2021	180	01-Nov-2025	178	31-Mar-2026	360	Jun/2028
	Comments on achieving targets		Progress on track. To date, 178 students (51% women) have graduated from the Rwanda Coding Academy and 70 more are expected to graduate by closing. A further 128 students (42% women) are currently pursuing advanced digital higher education degrees financed via the Student Loan Fund - 41 of which are expected to graduate by Dec 2025 and 51 by Dec 2026. The remaining students supported are graduating after project closing. BRD is exploring if there is scope to take on more student loans commitments.					
Of which female (Percentage)	0.00		51		47		35.00	
	Comments on achieving targets		Target surpassed. Supplemental Indicator. Share of graduates that are female.					
Startups reporting satisfaction with incubation services received (Percentage)	0.00	Dec/2021	0.00	01-Nov-2025	62.50	31-Mar-2026	75.00	Jun/2028
	Comments on achieving targets		Progress on tack. Performance-based grants for ecosystem support organizations (ESO) have been awarded, which is set to improve incubation services provided to digital start-ups, but start-ups have not yet been surveyed. A survey is under development that will allow all entrepreneurs supported through the ESOs to to be surveyed and results on this indicator to be delivered by December 2025. A second comparison survey will be conducted in					




		December 2026, prior to the end of the project.
--	--	---



7. DATA ON FINANCIAL PERFORMANCE

7.1 Cumulative Disbursements

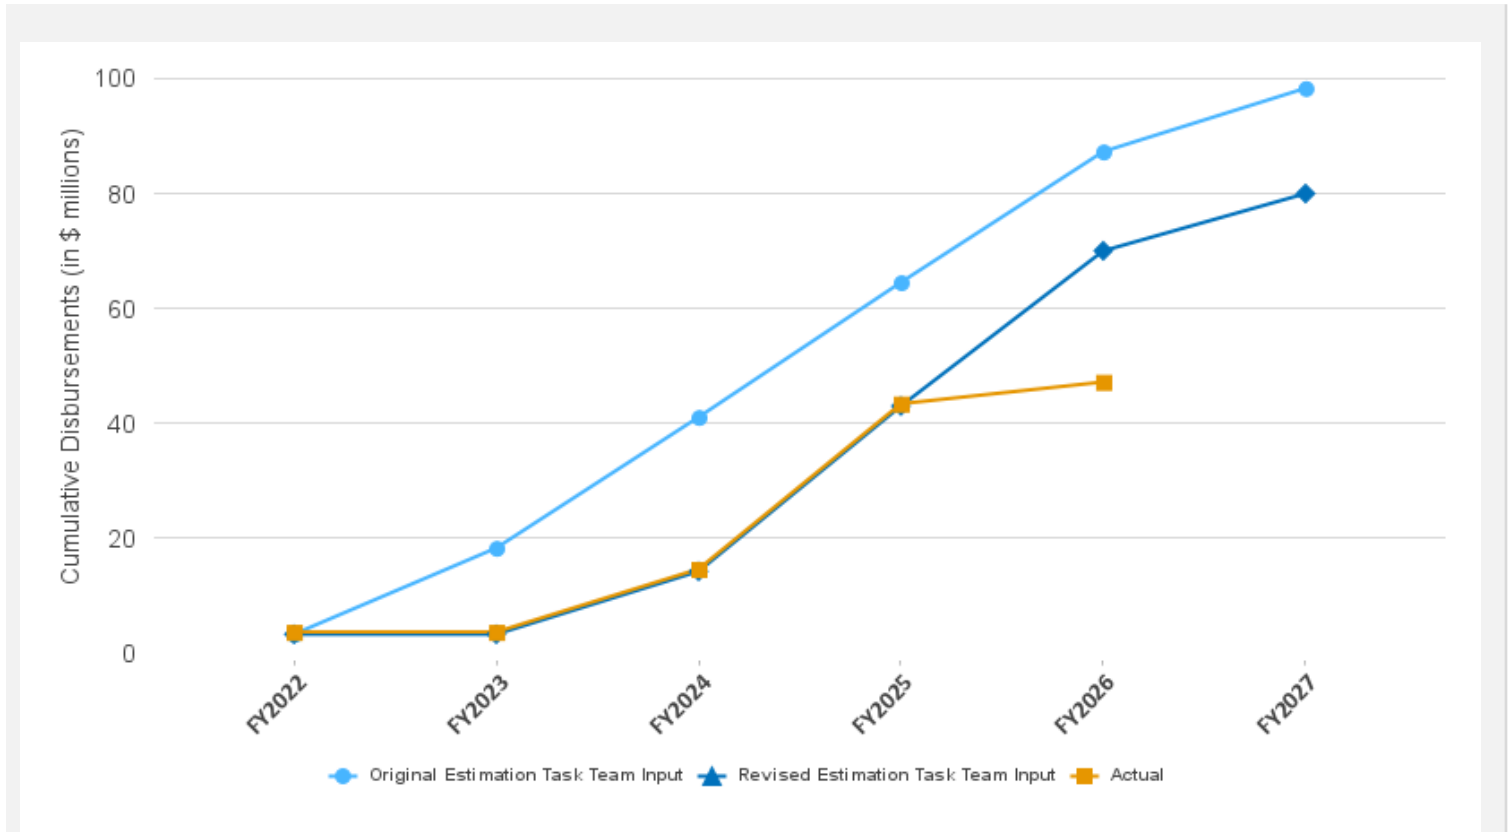

7.2 Disbursements (by loan)

Loan/Credit/TF	Status	Original	Revised	Cancelled	Disbursed	Undisbursed	Historical Disbursed	% Disbursed
COFN-C2100	Effective	100.00	101.31	0.00	43.46	57.86	0.00	42.90%
IDA-70000	Effective	100.00	79.73	21.58	49.68	30.05	0.00	62.31%
IDA-70000	Effective	0.00	0.00	0.00	0.00	0.00	0.00	0%
IDA-80220	Not Effective	20.00	19.91	0.00	0.00	19.91	0.00	0%



7.3 Key Dates (by loan)

Loan/Credit/TF	Status	Approval	Signing	Effectiveness	Orig. Closing	Rev. Closing
COFN-C2100	Effective	30-Nov-2021	20-Apr-2022	20-Apr-2022	31-Dec-2026	31-Dec-2026
IDA-70000	Effective	30-Nov-2021	07-Dec-2021	24-Mar-2022	31-Dec-2026	31-Dec-2026
IDA-70000	Effective	30-Nov-2021	07-Dec-2021	18-Mar-2026	31-Dec-2026	31-Dec-2026
IDA-70000	Effective	30-Nov-2021	07-Dec-2021	15-Apr-2026	31-Dec-2026	31-Dec-2026
IDA-80220	Not Effective	30-Mar-2026			30-Jun-2028	30-Jun-2028

8. KEY DATES

Key Events	Planned	Actual
Approval	30-Nov-2021	30-Nov-2021
Effectiveness	24-Mar-2022	24-Mar-2022
Mid-Term Review No. 01	18-Oct-2024	18-Oct-2024
Operation Closing/Cancellation	30-Jun-2028	

9. RESTRUCTURING HISTORY

Restructuring Level 2 Approved on 20-Dec-2023
Restructuring Level 2 Approved on 11-Aug-2025
Restructuring Level 2 Approved on 10-Jun-2024

10. ASSOCIATED OPERATION(S)

There are no associated operations
